

UTM MAJOR CAPITAL PROJECTS: Status Report

UTM Campus Council
May 19, 2021



CAMPUS MASTER PLAN

End date for project is June 2021

Campus Master Plan Process



Note: Changes to project timeline and consultation methods may occur to reflect the evolution of COVID-19.

MAJOR CAPITAL PROJECTS

Level 2 (\$5-\$20 Million)


- Student Services Hub (SSH)
- Robotic Laboratory Environments (RLE)



STUDENT SERVICES HUB (SSH)

Project timeline

- In design
- Tender and Award:
October 2021
- Construction start:
December 2021
- Occupancy:
February 2023

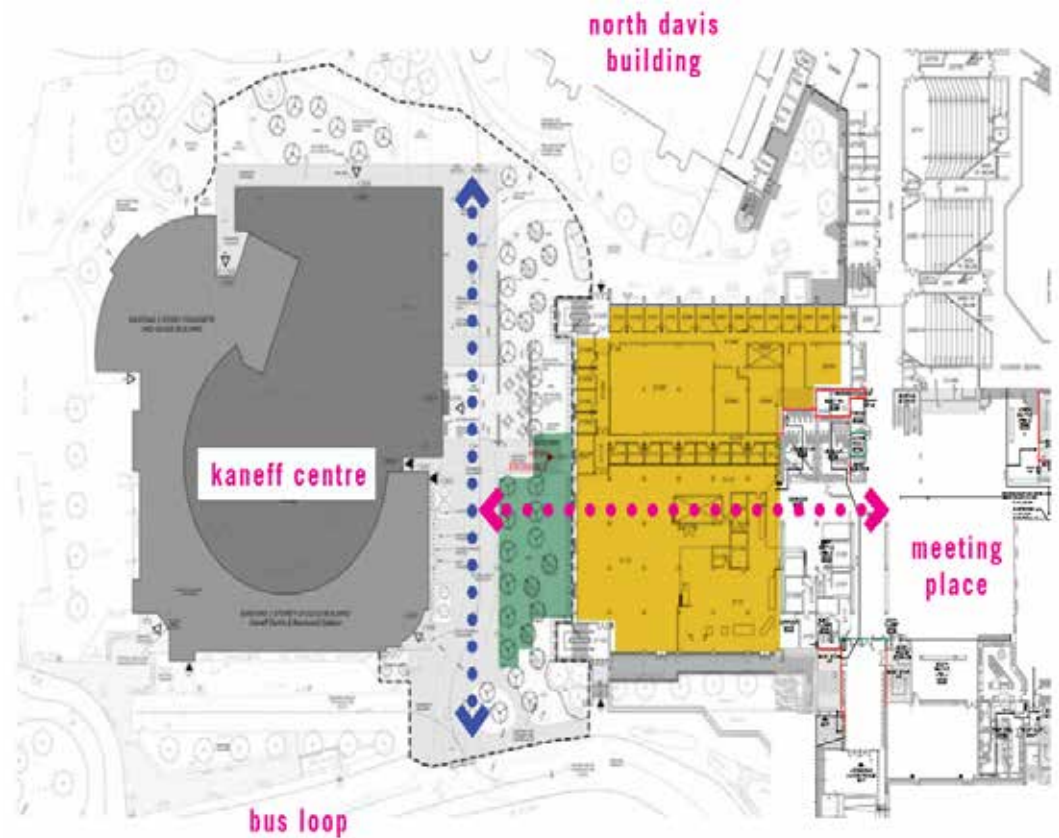

ROBOTICS LABORATORY ENVIRONMENTS (RLE)

Project Timeline:

- Design and Costing: April 2020 - August 2021
- Tender and Award: late Fall 2021
- **Occupancy: Fall 2022**



MAJOR CAPITAL PROJECTS

Level 3 (\$20+ Million)

- New Science Building (NSB)
- Arts, Culture and Technology (ACT)
- New Residence



NEW SCIENCE BUILDING (NSB)

Project status

- Governance approval: Dec. 14, 2017
- Architect award: March 2018
- Design & Tender: ended Nov. 2019
- Construction Contract Award: March 2020
- **Occupancy Target: 2023**



ARTS, CULTURE AND TECHNOLOGY (ACT)



Project timeline

- Design and Costing: Feb. 2020 – Feb. 2022
- Tender and Award: March 2022
- **Occupancy: Spring 2025**

NEW RESIDENCE

Project Timeline

- Design and Costing: Nov. 2020 - March 2022
- Tender and Award: Mid-March - May 2022
- Occupancy: June 2024

